

OPERATIONS REVIEW

Cutting changeover time on Line 4

What we changed, what it delivered, and what we need next.

Agenda

01	Where we started	3
02	What we changed	5
03	Results so far	7
04	Decision needed	10

01

Where we started

Changeovers were the largest single source of lost capacity.

01 · BASELINE

Changeovers cost us almost a shift every week

94 min

Average changeover

Target: 45 min

11

Changeovers per week

Up from 7 last year

17 h


Capacity lost weekly

≈ 2 shifts

Source: Line 4 MES data, Jan–Mar, illustrative

02 · METHOD

We moved setup work outside the stoppage

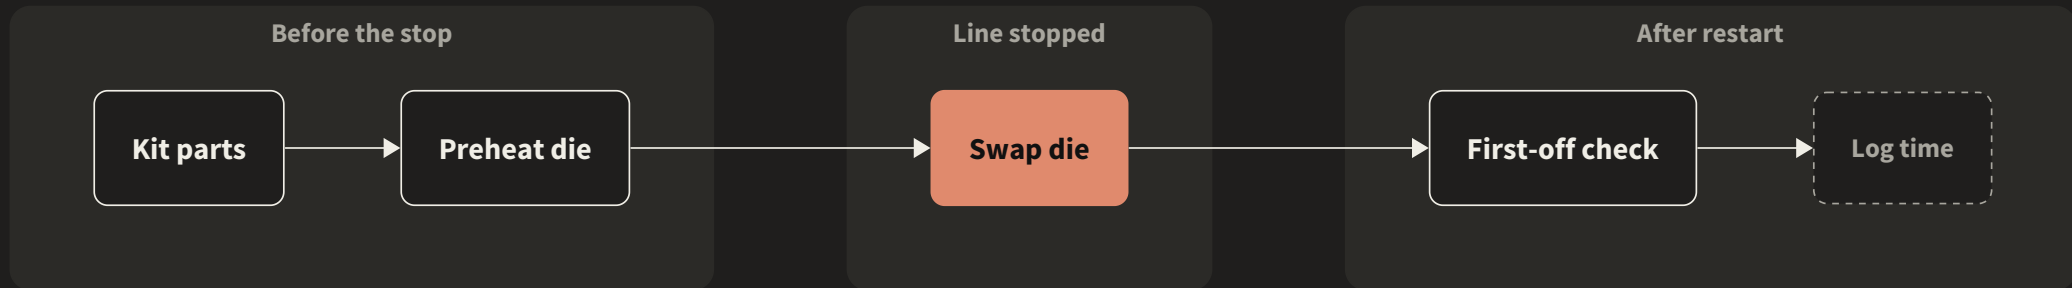

Only the highlighted step still needs the line stopped.

02 · METHOD

A four-step method made the gain repeatable

1

Film

Record three changeovers.

2

Split

Mark each task internal or external.

3

Shift

Move external tasks ahead of the stop.

4

Standardise


Kit carts, checklists, quick clamps.

LESSON

Kitting delivered the biggest gain.

03 · RESULTS

Changeover time fell 41% in eight weeks

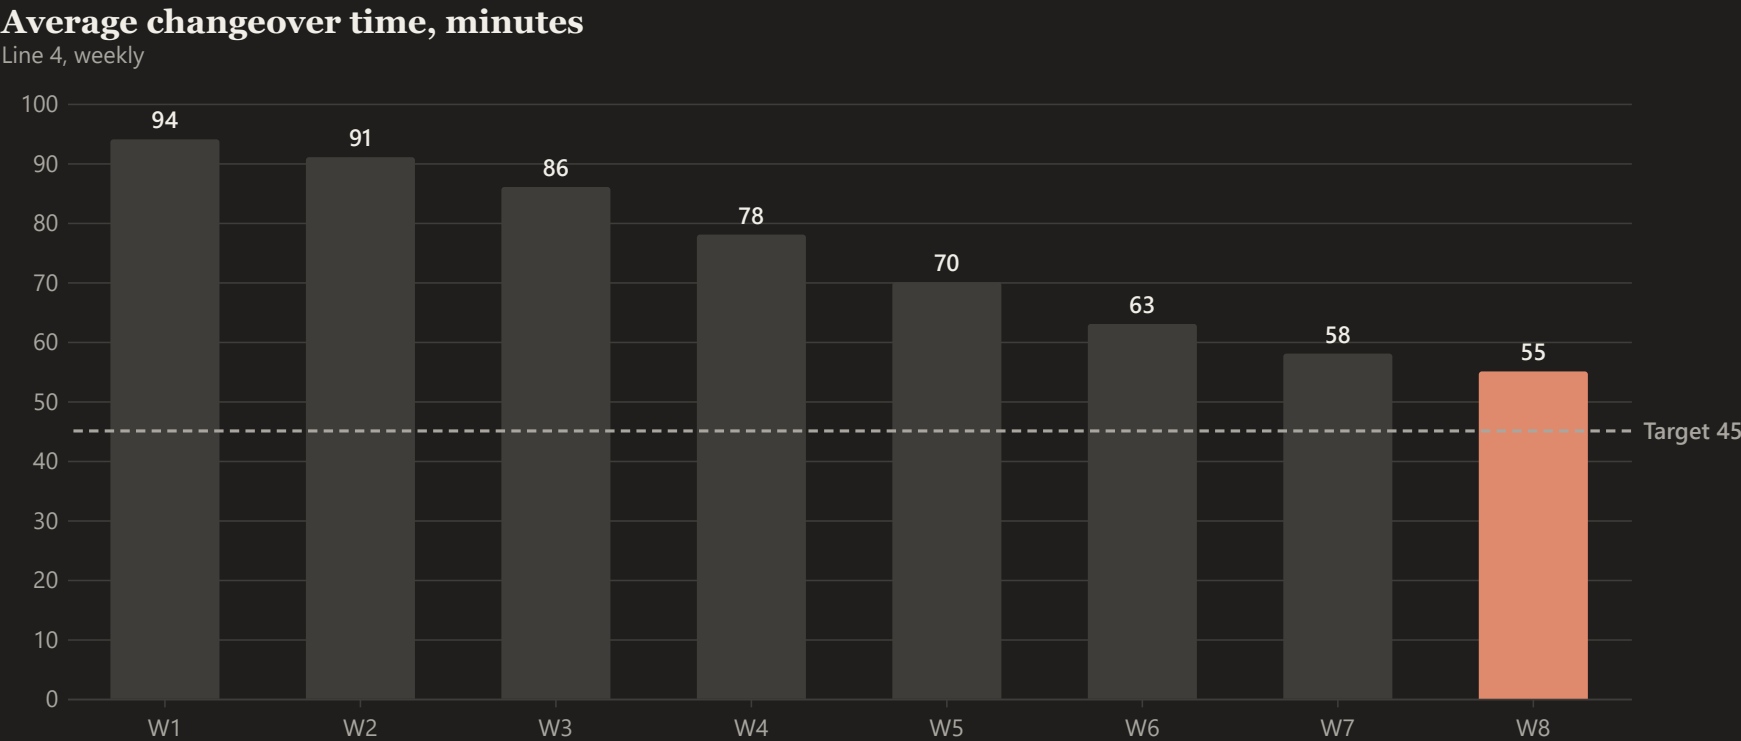

Source: Line 4 MES, weekly average, illustrative

03 · RESULTS

Only Line 5 still worsens

LINE	BEFORE	NOW	CHANGE	STATUS
Line 2	88 min	71 min	-19%	WATCH
Line 3	102 min	84 min	-18%	WATCH
Line 4	94 min	55 min	-41%	GOOD
Line 5	79 min	81 min	+3%	OFF TRACK

03 · RESULTS

Write the standard so anyone can follow it

DO

Torque clamps to 40 Nm, then verify with the gauge on cart B.

DON'T

Tighten the clamps properly before restarting.

Kitting delivered **more than half** of
the gain — and costs almost nothing.

04 · DECISION

Expand to three lines by Q3



Q1

Line 4 pilot



Q2

Kit carts for Lines 2–3



Q3

Line 5 and training



Q4

Audit and sustain

☒ Pilot results reviewed with plant leadership

☐ Approve €40k for six kit carts

☐ Name a changeover lead per line

DECISION NEEDED

Approve the Q3 roll-out?
