

OPERATIONS REVIEW

Cutting changeover time on Line 4

What we changed, what it delivered, and what we need next.

Agenda

01	Where we started	3
02	What we changed	5
03	Results so far	7
04	Decision needed	10

01

Where we started

Changeovers were the largest single source of lost capacity.

01 · BASELINE

Changeovers cost us almost a shift every week

94 min

Average changeover

Target: 45 min

11

Changeovers per week

Up from 7 last year

17 h


Capacity lost weekly

≈ 2 shifts

Source: Line 4 MES data, Jan–Mar, illustrative

02 · METHOD

We moved setup work outside the stoppage

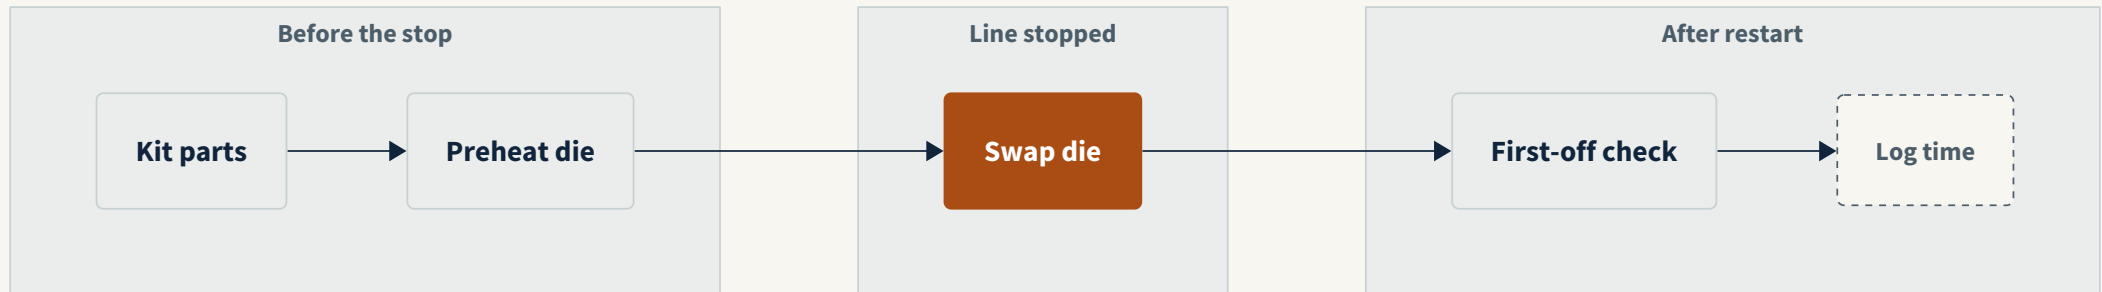

Only the highlighted step still needs the line stopped.

02 · METHOD

A four-step method made the gain repeatable

1

Film

Record three changeovers.

2

Split

Mark each task internal or external.

3

Shift

Move external tasks ahead of the stop.

4

Standardise

Kit carts, checklists, quick clamps.

LESSON


Kitting delivered the biggest gain.

03 · RESULTS

Changeover time fell 41% in eight weeks

Average changeover time, minutes

Line 4, weekly

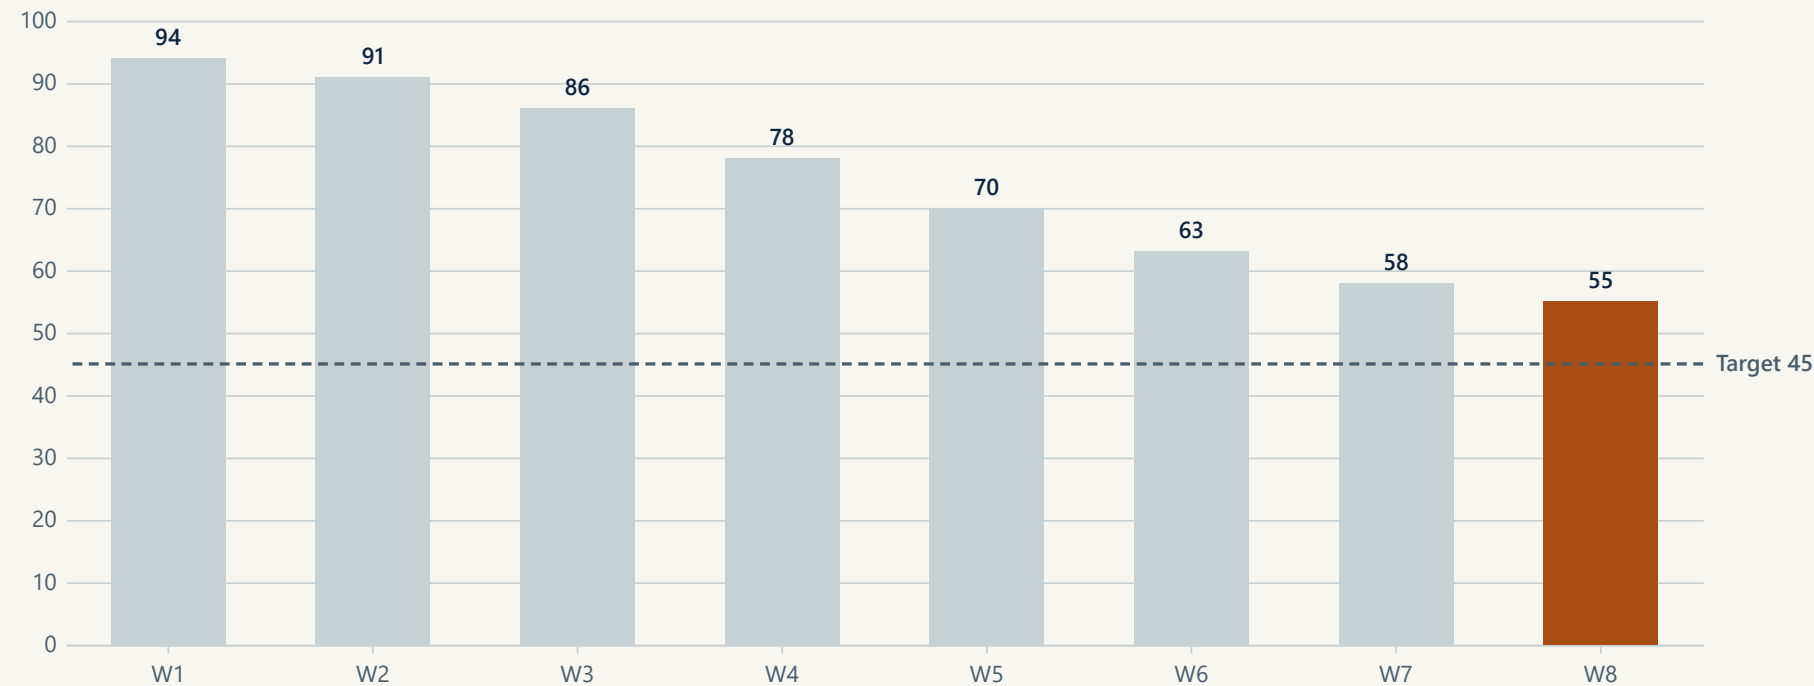

Source: Line 4 MES, weekly average, illustrative

03 · RESULTS

Only Line 5 still worsens

LINE	BEFORE	NOW	CHANGE	STATUS
Line 2	88 min	71 min	–19%	WATCH
Line 3	102 min	84 min	–18%	WATCH
Line 4	94 min	55 min	–41%	GOOD
Line 5	79 min	81 min	+3%	OFF TRACK

03 · RESULTS

Write the standard so anyone can follow it

DO

Torque clamps to 40 Nm, then verify with the gauge on cart B.


DON'T

Tighten the clamps properly before restarting.

**Kitting delivered more
than half of the gain —
and costs almost nothing.**

04 · DECISION

Expand to three lines by Q3



- ☒ Pilot results reviewed with plant leadership
- ☐ Approve €40k for six kit carts
- ☐ Name a changeover lead per line

DECISION NEEDED

Approve the Q3 roll-out?
